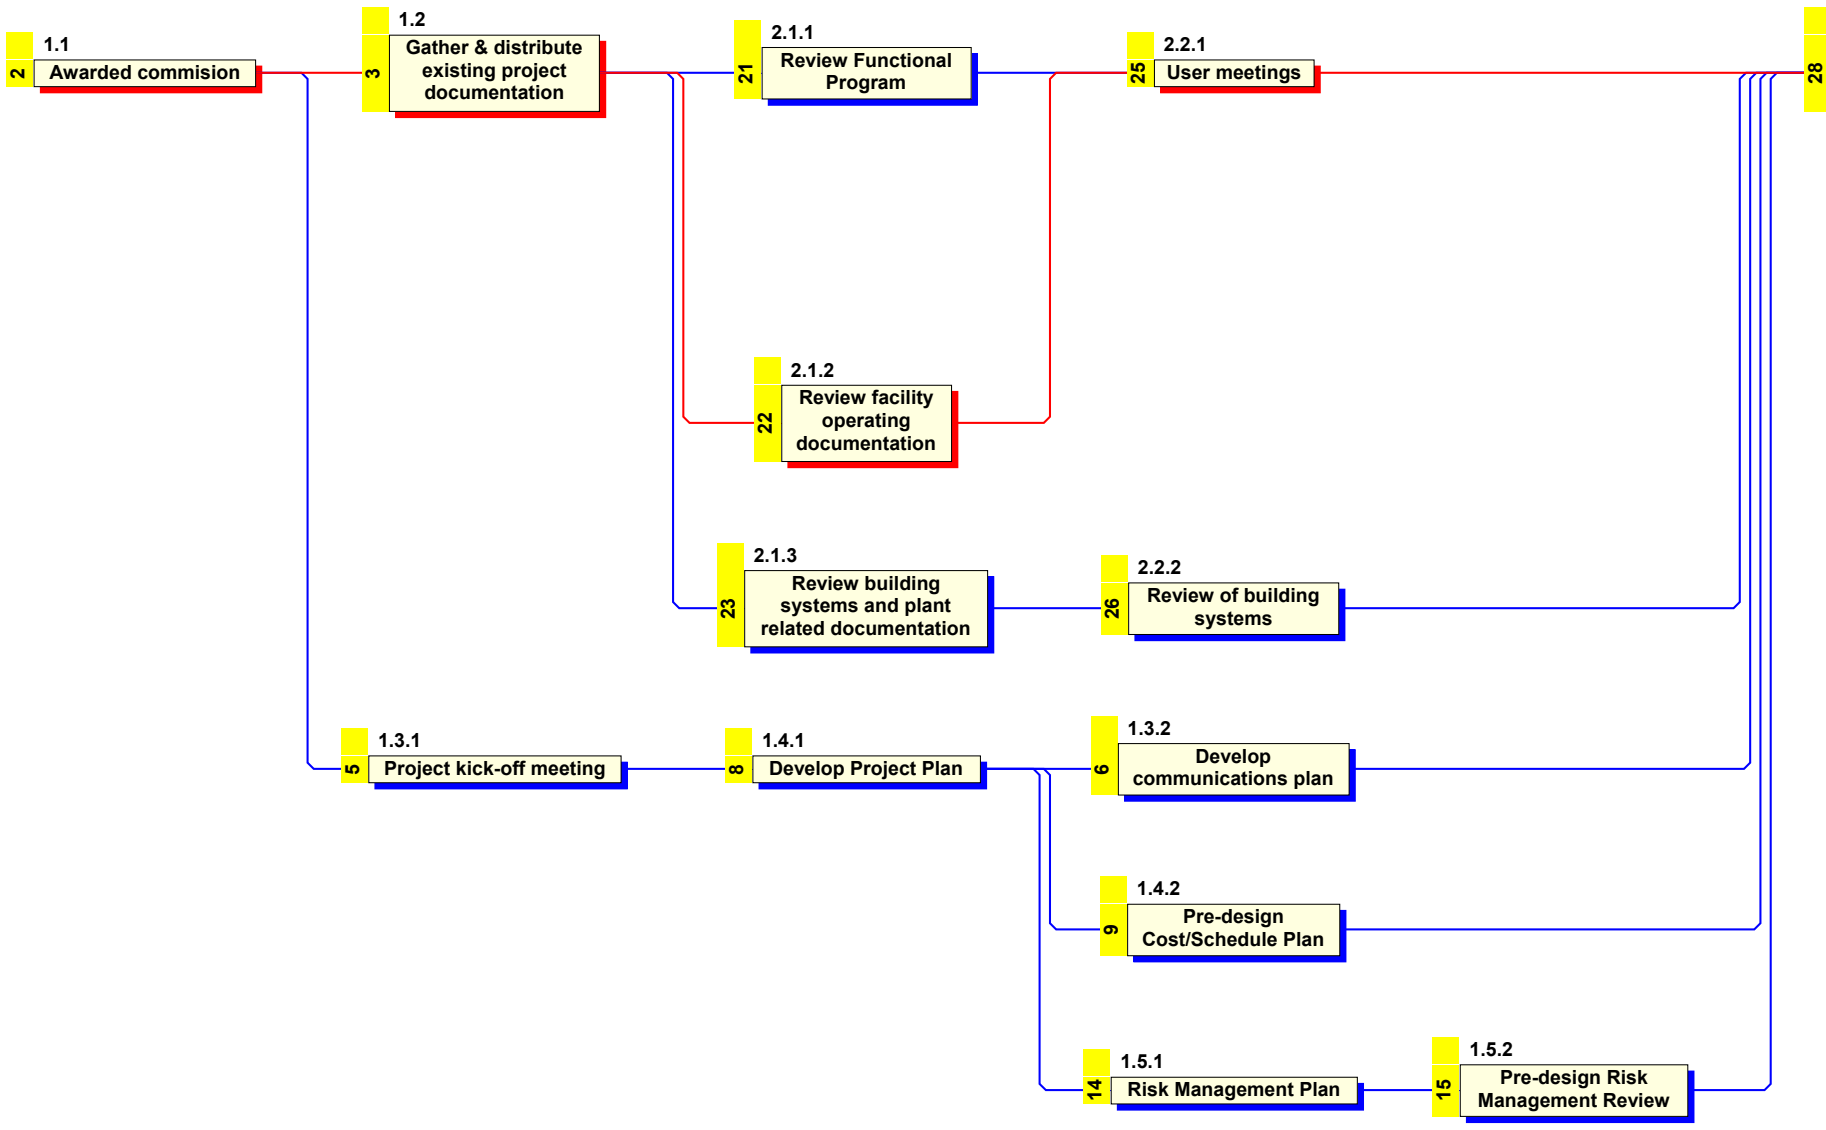
2
1.1
Awarded commision
3
1.2
Gather & distribute existing project documentation
21
2.1.1
Review Functional Program
25
2.2.1
User meetings
28
22
2.1.2
Review facility operating documentation
23
2.1.3
Review building systems and plant related documentation
26
2.2.2
Review of building systems
5
1.3.1
Project kick-off meeting
8
1.4.1
Develop Project Plan
6
1.3.2
Develop communications plan
9
1.4.2
Pre-design Cost/Schedule Plan
14
1.5.1
Risk Management Plan
15
1.5.2
Pre-design Risk Management Review

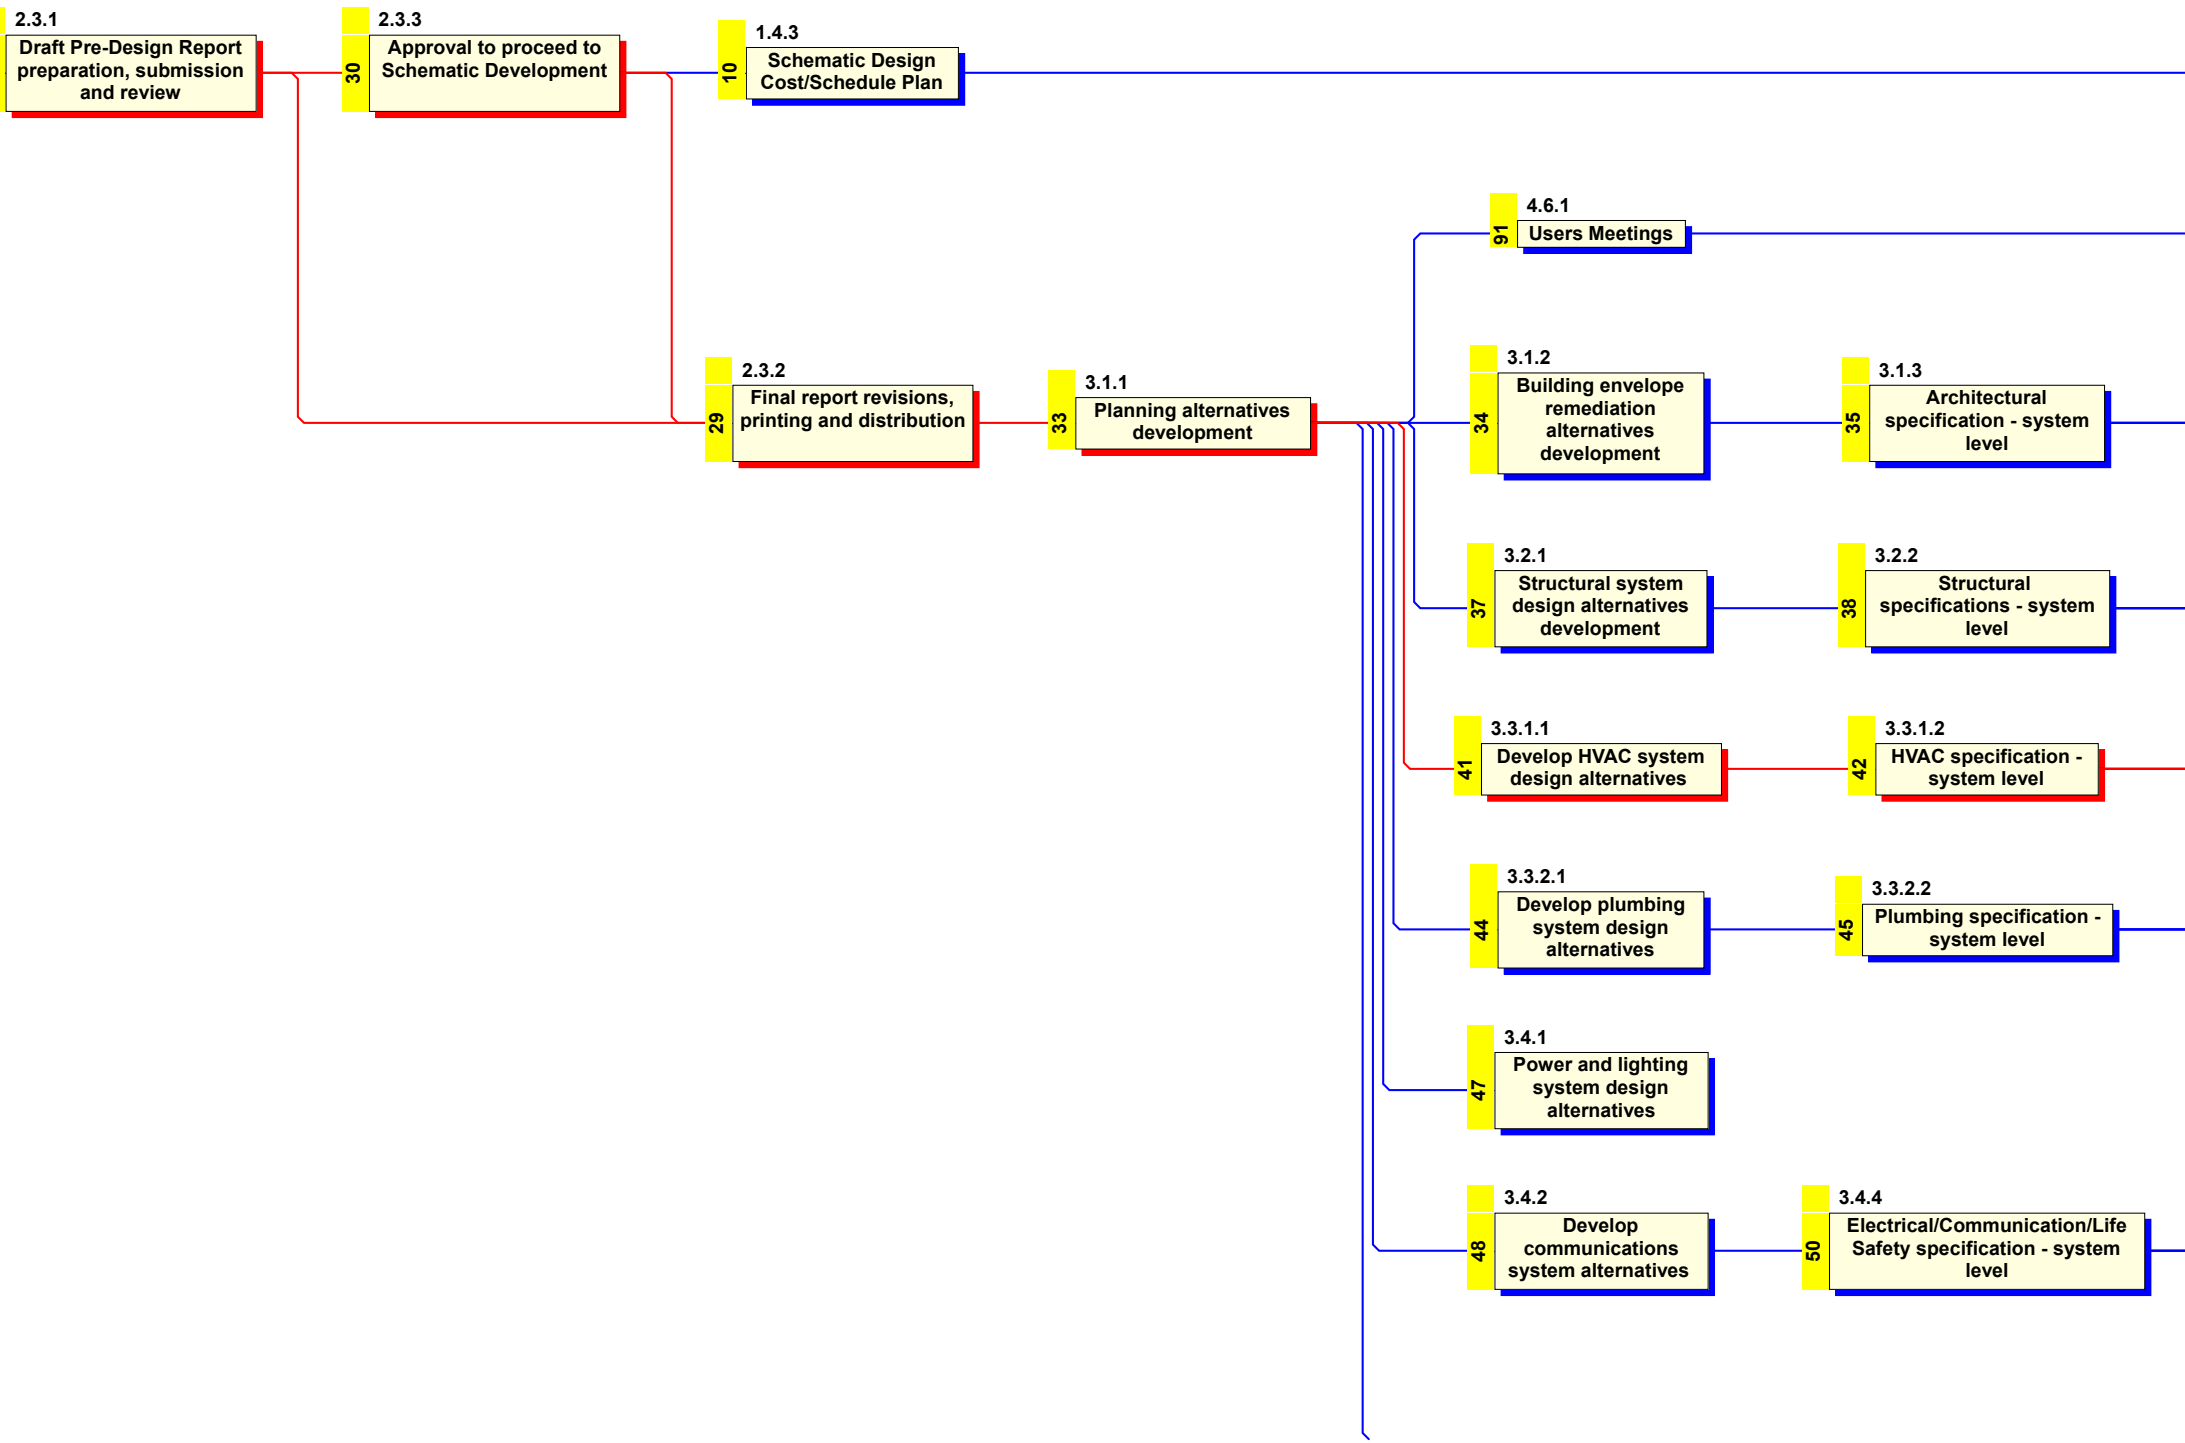
2.3.1
Draft Pre-Design Report preparation, submission and review
2.3.3
30
Approval to proceed to Schematic Development
1.4.3
10
Schematic Design Cost/Schedule Plan
4.6.1
91
Users Meetings
2.3.2
29
Final report revisions, printing and distribution
3.1.1
33
Planning alternatives development
3.1.2
34
Building envelope remediation alternatives development
3.1.3
35
Architectural specification - system level
3.2.1
37
Structural system design alternatives development
3.2.2
38
Structural specifications - system level
3.3.1.1
41
Develop HVAC system design alternatives
3.3.1.2
42
HVAC specification - system level
3.3.2.1
44
Develop plumbing system design alternatives
3.3.2.2
45
Plumbing specification - system level
3.4.1
47
Power and lighting system design alternatives
3.4.2
48
Develop communications system alternatives
3.4.4
50
Electrical/Communication/Life Safety specification - system level

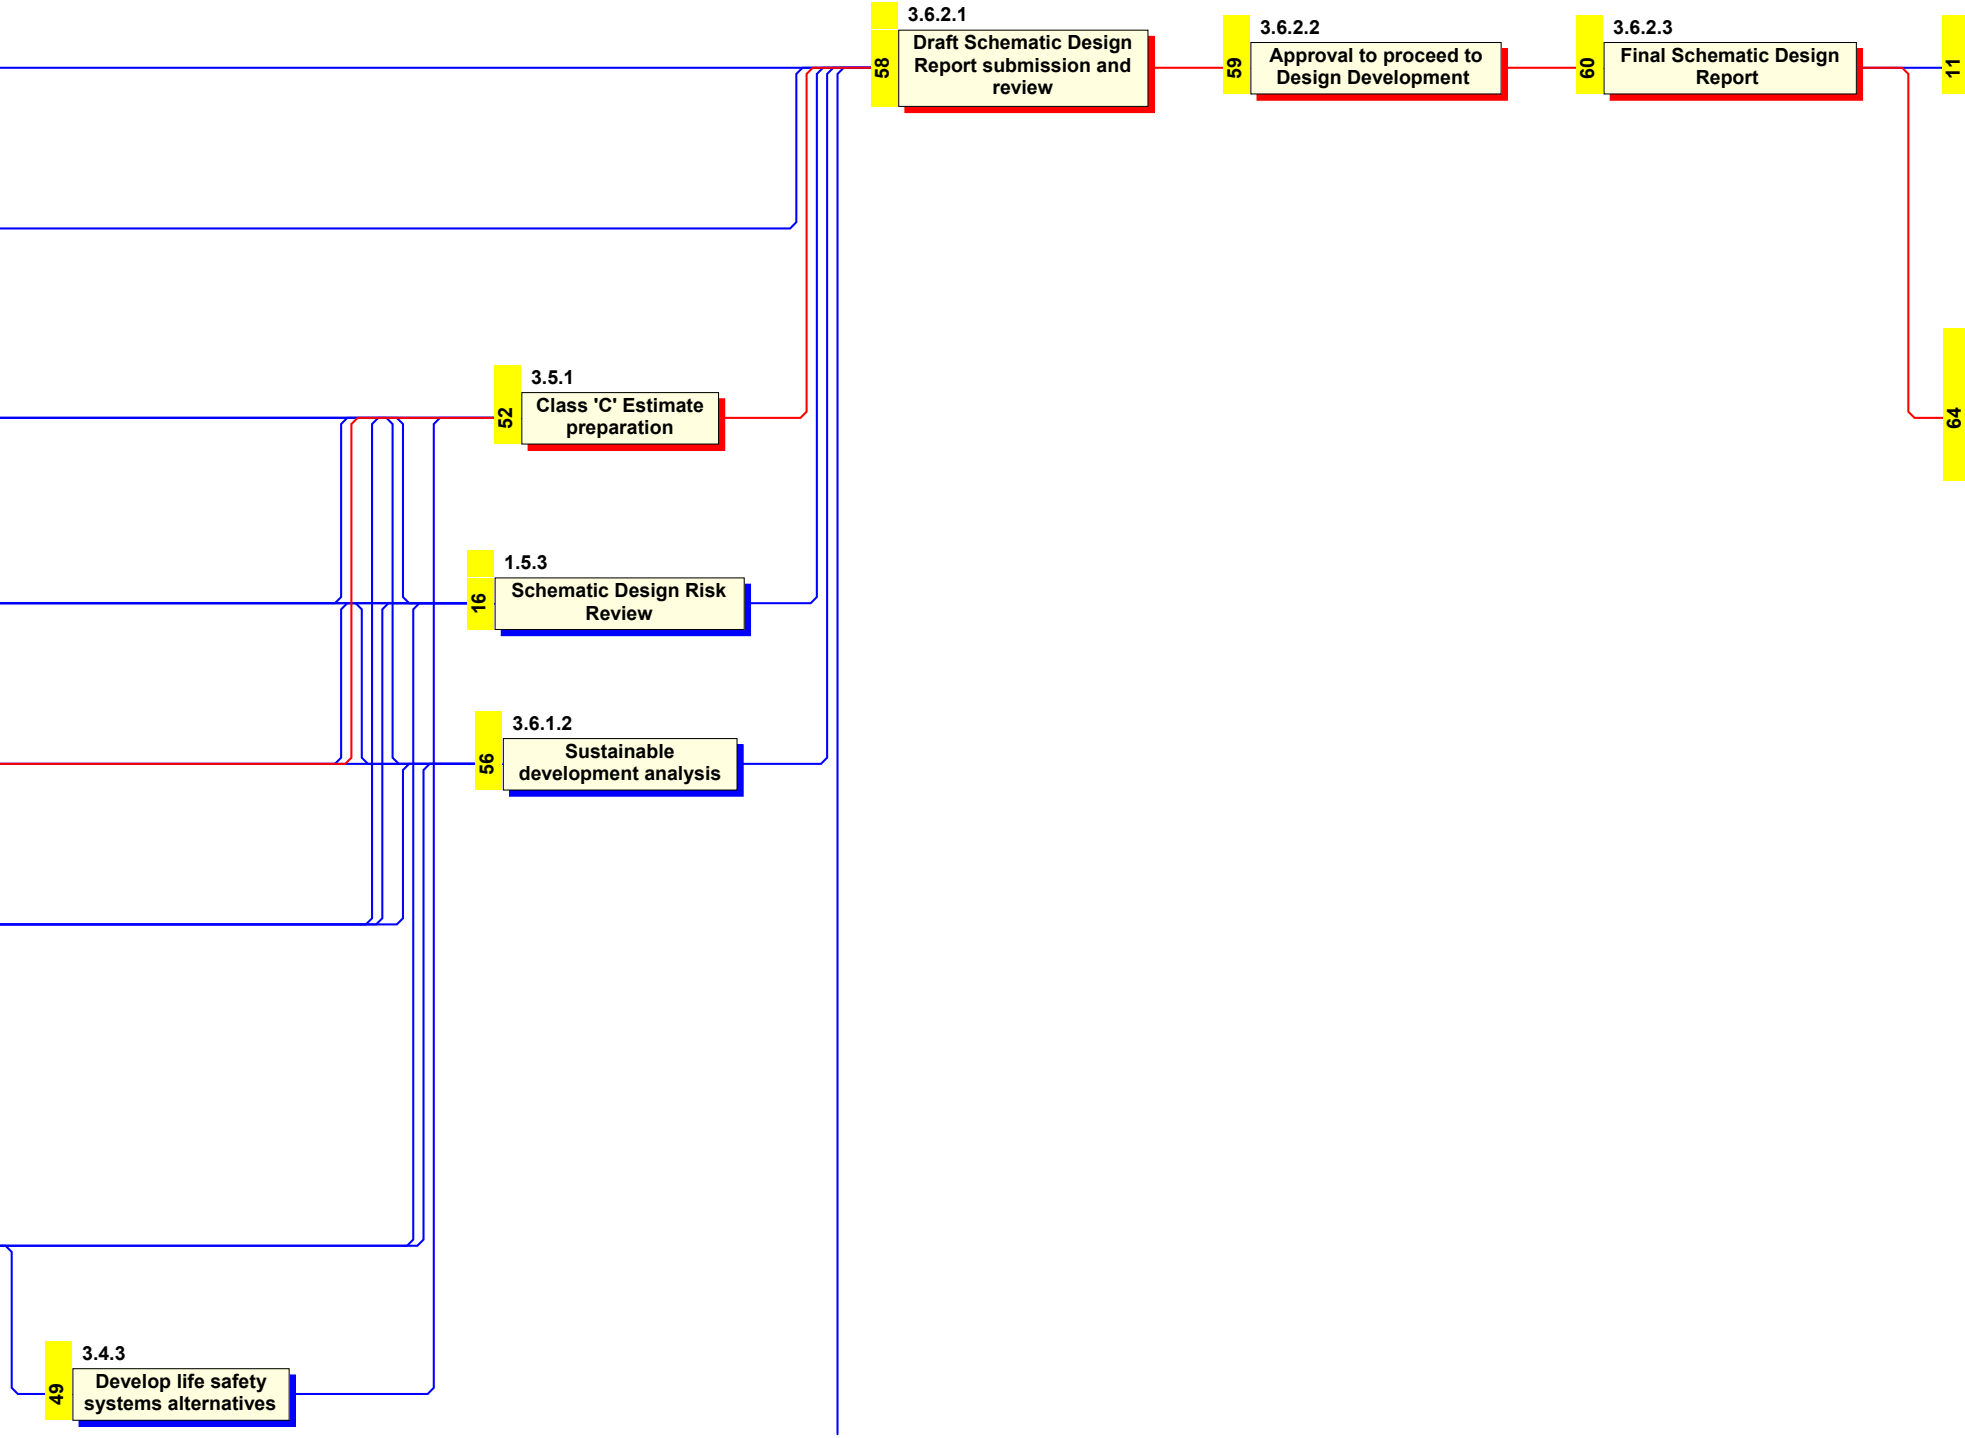
3.6.2.1
58
Draft Schematic Design Report submission and review
3.6.2.2
59
Approval to proceed to Design Development
3.6.2.3
60
Final Schematic Design Report
11
3.5.1
52
Class 'C' Estimate preparation
64
1.5.3
16
Schematic Design Risk Review
3.6.1.2
56
Sustainable development analysis
3.4.3
49
Develop life safety systems alternatives

Elementary School - Addition and Alterations - Network Diagram

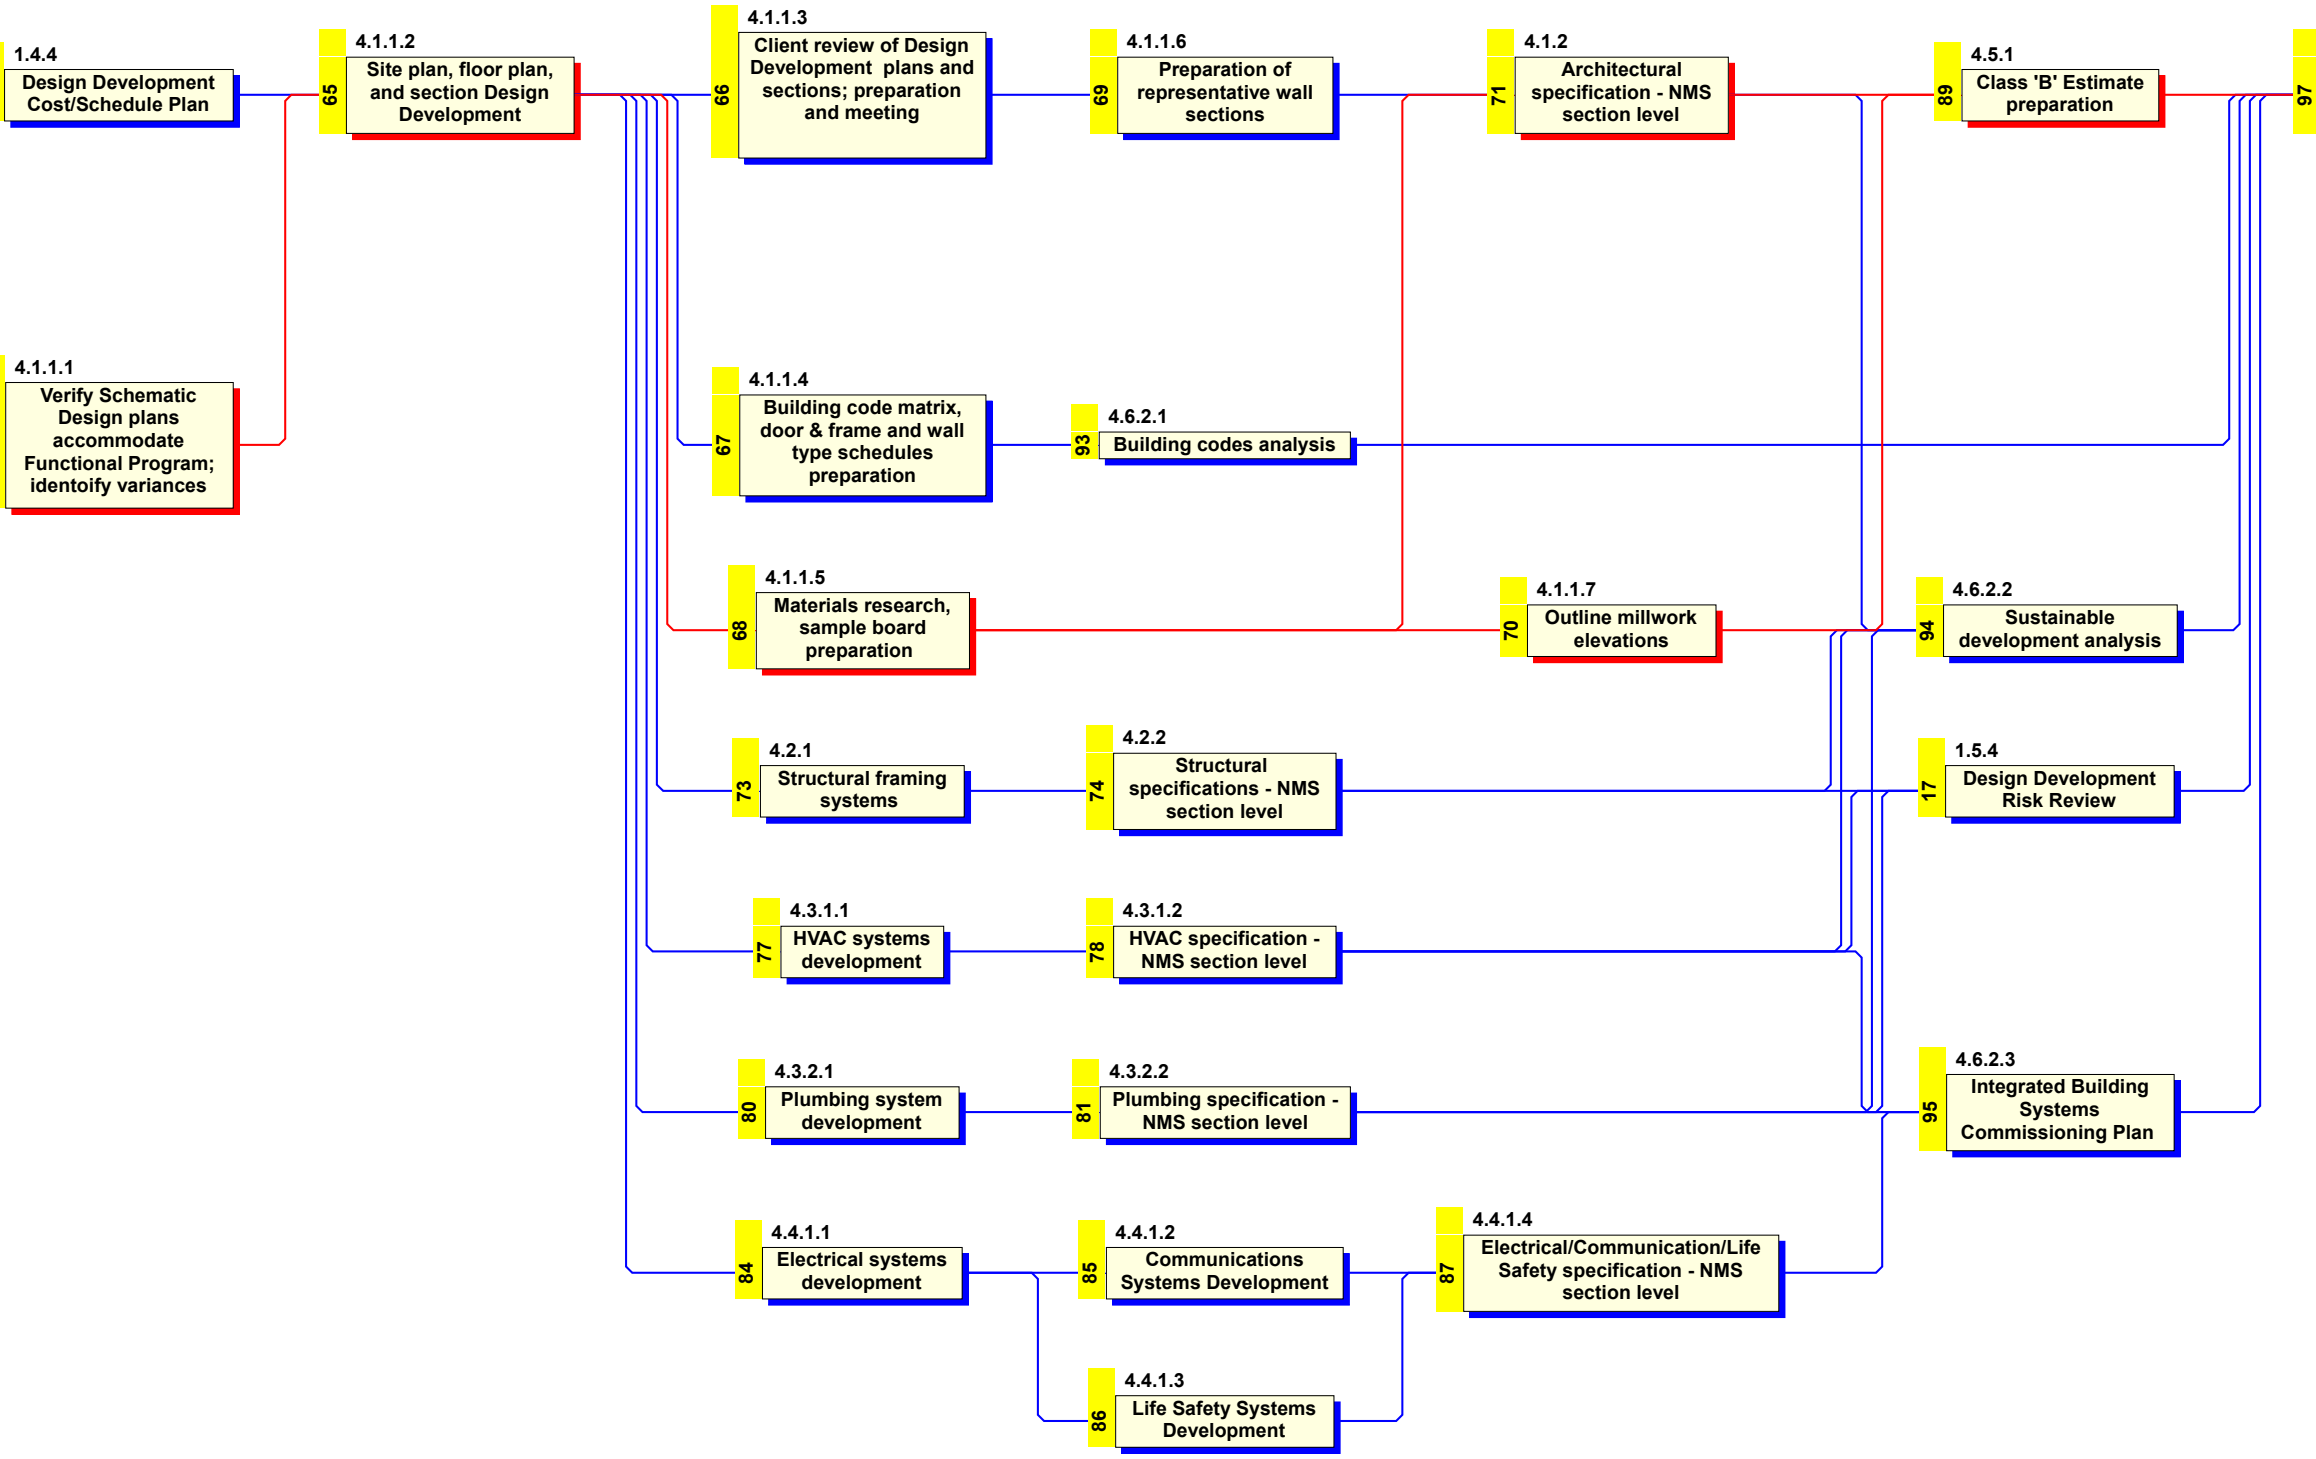
1.4.4
Design Development Cost/Schedule Plan
4.1.1.1
Verify Schematic Design plans accommodate Functional Program; identoify variances
4.1.1.2
65
Site plan, floor plan, and section Design Development
4.1.1.3
66
Client review of Design Development plans and sections; preparation and meeting
4.1.1.4
67
Building code matrix, door & frame and wall type schedules preparation
4.1.1.5
68
Materials research, sample board preparation
4.2.1
73
Structural framing systems
4.3.1.1
77
HVAC systems development
4.3.2.1
80
Plumbing system development
4.4.1.1
84
Electrical systems development
4.1.1.6
69
Preparation of representative wall sections
4.6.2.1
93
Building codes analysis
4.2.2
74
Structural specifications - NMS section level
4.3.1.2
78
HVAC specification - NMS section level
4.3.2.2
81
Plumbing specification - NMS section level
4.4.1.2
85
Communications Systems Development
4.4.1.3
86
Life Safety Systems Development
4.1.2
71
Architectural specification - NMS section level
4.1.1.7
70
Outline millwork elevations
4.4.1.4
87
Electrical/Communication/Life Safety specification - NMS section level
4.5.1
89
Class 'B' Estimate preparation
4.6.2.2
94
Sustainable development analysis
1.5.4
17
Design Development Risk Review
4.6.2.3
95
Integrated Building Systems Commissioning Plan
97

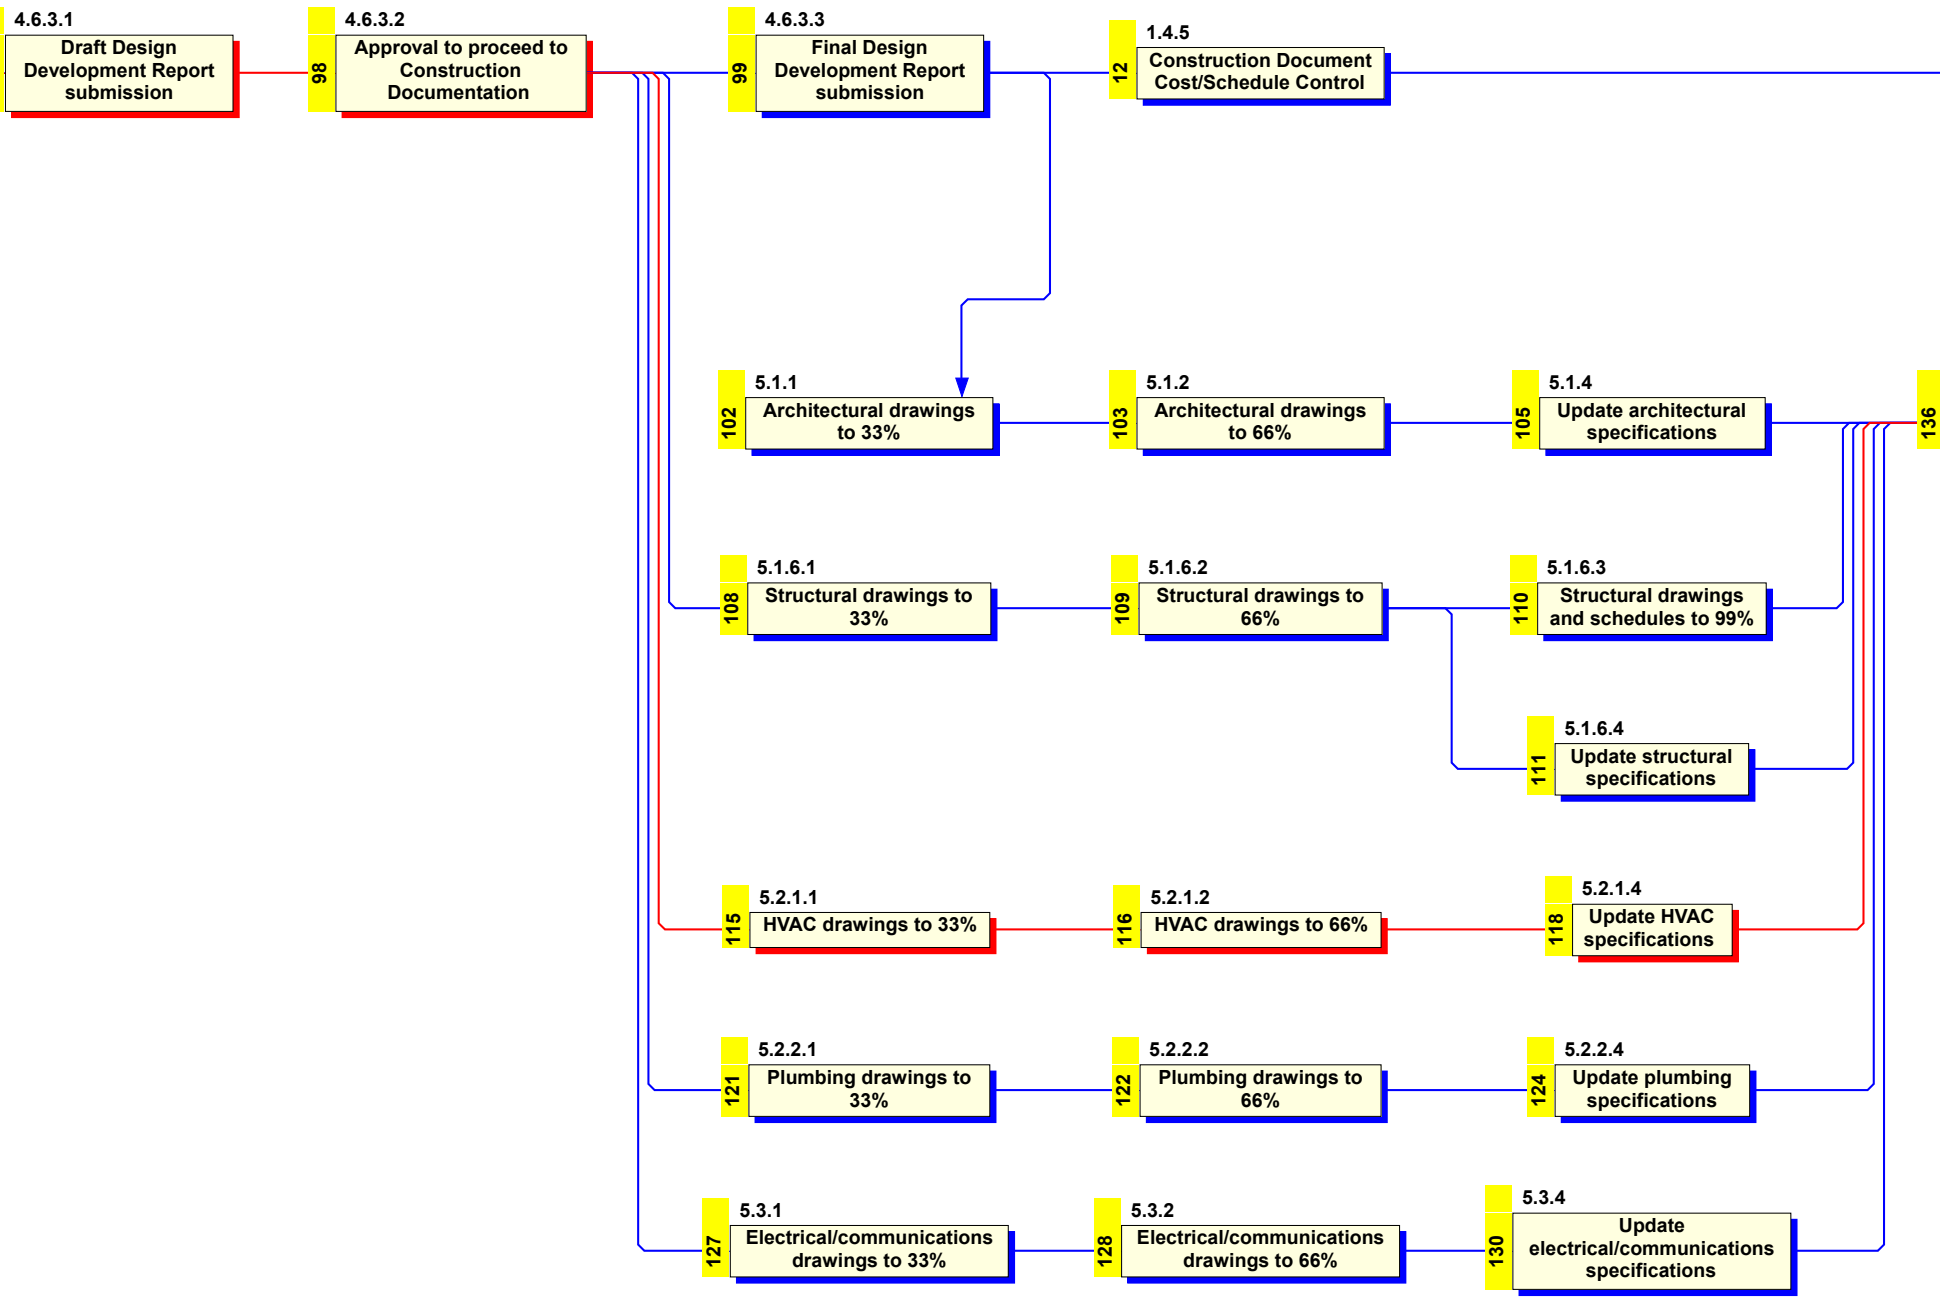
4.6.3.1
Draft Design Development Report submission
98
4.6.3.2
Approval to proceed to Construction Documentation
99
4.6.3.3
Final Design Development Report submission
12
1.4.5
Construction Document Cost/Schedule Control
102
5.1.1
Architectural drawings to 33%
103
5.1.2
Architectural drawings to 66%
105
5.1.4
Update architectural specifications
136
108
5.1.6.1
Structural drawings to 33%
109
5.1.6.2
Structural drawings to 66%
110
5.1.6.3
Structural drawings and schedules to 99%
111
5.1.6.4
Update structural specifications
115
5.2.1.1
HVAC drawings to 33%
116
5.2.1.2
HVAC drawings to 66%
118
5.2.1.4
Update HVAC specifications
121
5.2.2.1
Plumbing drawings to 33%
122
5.2.2.2
Plumbing drawings to 66%
124
5.2.2.4
Update plumbing specifications
127
5.3.1
Electrical/communications drawings to 33%
128
5.3.2
Electrical/communications drawings to 66%
130
5.3.4
Update electrical/communications specifications

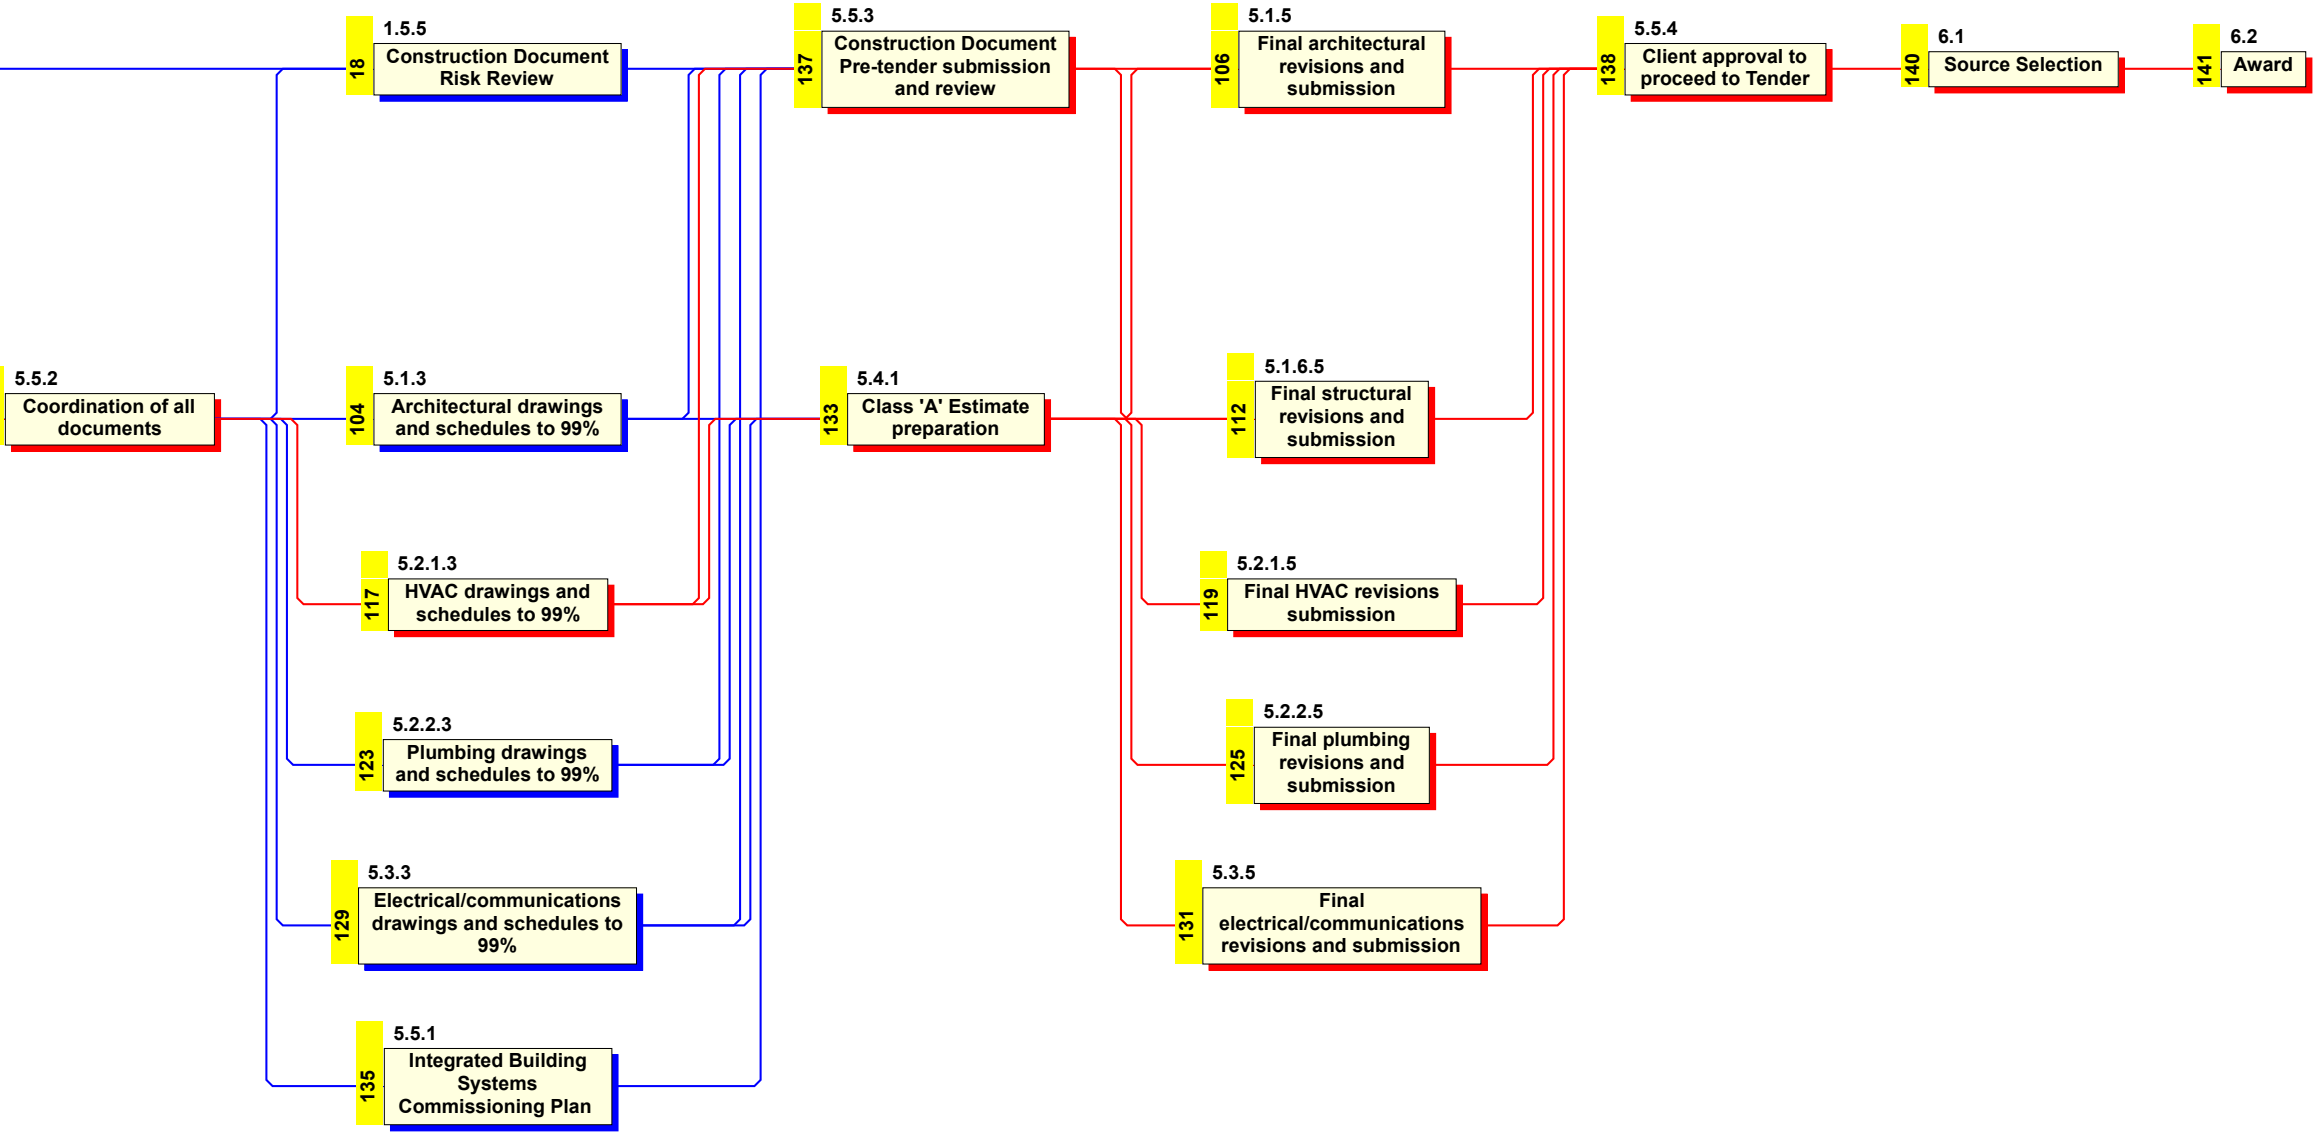
1.5.5
18
Construction Document Risk Review
5.5.3
137
Construction Document Pre-tender submission and review
5.1.5
106
Final architectural revisions and submission
5.5.4
138
Client approval to proceed to Tender
6.1
140
Source Selection
6.2
141
Award
5.5.2
Coordination of all documents
5.1.3
104
Architectural drawings and schedules to 99%
5.4.1
133
Class 'A' Estimate preparation
5.1.6.5
112
Final structural revisions and submission
5.2.1.3
117
HVAC drawings and schedules to 99%
5.2.1.5
119
Final HVAC revisions submission
5.2.2.3
123
Plumbing drawings and schedules to 99%
5.2.2.5
125
Final plumbing revisions and submission
5.3.3
129
Electrical/communications drawings and schedules to 99%
5.3.5
131
Final electrical/communications revisions and submission
5.5.1
135
Integrated Building Systems Commissioning Plan
